



Weatherford[®]

Completion Systems

DRILL STEM TEST REPORT

Prepared For: **Berexco LLC**

2020 N. Bramblewood
Wichita KS 67206-1094

ATTN: Bruce Meyer

10-11s-19w Ellis,KS

Armbrister Unit #1

Start Date: 2010.10.04 @ 20:33:43

End Date: 2010.10.05 @ 04:45:13

Job Ticket #: 090406 DST #: 3

ALPINE OIL SERVICES CORPORATION
2460, 240 - 4 Avenue S.W. Calgary, AB. T2P 4H4
ph: 263-7800 fax: 264-7260



Weatherford[®] Completion Systems

DRILL STEM TEST REPORT

Berexco LLC
2020 N. Bramblewood
Wichita KS 67206-1094
ATTN: Bruce Meyer

Armbrister Unit #1
10-11s-19w Ellis,KS
Job Ticket: 090406 **DST#: 3**
Test Start: 2010.10.04 @ 20:33:43


GENERAL INFORMATION:

Formation: **LKC-"B-F"**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 22:58:43
Time Test Ended: 04:45:13
Interval: **3285.00 ft (KB) To 3365.00 ft (KB) (TVD)**
Total Depth: 3365.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Good
Test Type: Conventional Bottom Hole
Tester: Jeff Brown
Unit No: 44
Reference Elevations: 2074.00 ft (KB)
2069.00 ft (CF)
KB to GR/CF: 5.00 ft

Serial #: 8321 Inside
Press @ Run Depth: 262.67 psig @ 3289.00 ft (KB) Capacity: 8000.00 psig
Start Date: 2010.10.04 End Date: 2010.10.05 Last Calib.: 2010.10.05
Start Time: 20:33:44 End Time: 04:45:13 Time On Btm: 2010.10.04 @ 22:58:13
Time Off Btm: 2010.10.05 @ 02:48:43

TEST COMMENT: IFP-Good blow BOB in 13 min
ISI-Dead no blow back
FFP-Good blow BOB in 26 min
FSI-Dead no blow back

PRESSURE SUMMARY

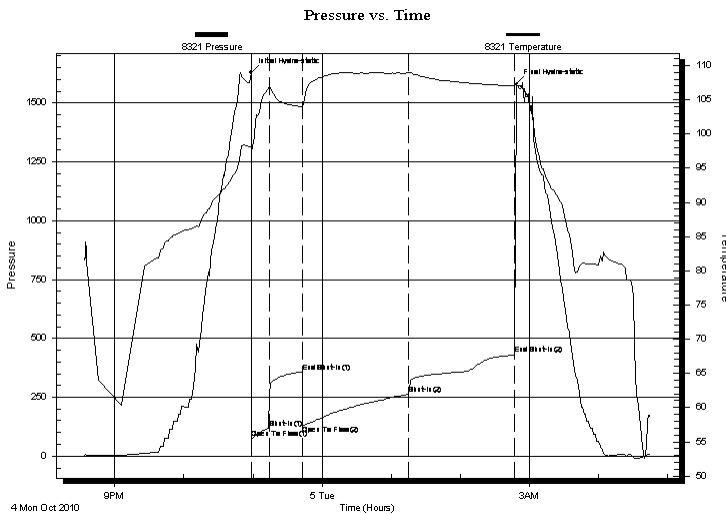

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1629.38	98.04	Initial Hydro-static
1	77.66	97.47	Open To Flow (1)
16	119.32	106.80	Shut-In(1)
45	357.26	103.96	End Shut-In(1)
45	130.13	103.84	Open To Flow (2)
137	262.67	108.96	Shut-In(2)
229	431.77	107.03	End Shut-In(2)
231	1581.45	107.09	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
362.00	MW40%M60%W	1.78
82.00	WM40%W60%M	0.89

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)



Weatherford
Completion Systems

DRILL STEM TEST REPORT

TOOL DIAGRAM

Berexco LLC
2020 N. Bramblewood
Wichita KS 67206-1094
ATTN: Bruce Meyer

Armbrister Unit #1
10-11s-19w Ellis,KS
Job Ticket: 090406 **DST#: 3**
Test Start: 2010.10.04 @ 20:33:43

Tool Information

Drill Pipe:	Length: 2924.00 ft	Diameter: 3.34 inches	Volume: 31.69 bbl	Tool Weight: 2200.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 2.70 inches	Volume: 0.00 bbl	Weight set on Packer: 25000.00 lb
Drill Collar:	Length: 362.00 ft	Diameter: 2.25 inches	Volume: 1.78 bbl	Weight to Pull Loose: 64000.00 lb
			<u>Total Volume: 33.47 bbl</u>	Tool Chased 0.00 ft
Drill Pipe Above KB:	29.00 ft			String Weight: Initial 50000.00 lb
Depth to Top Packer:	3285.00 ft			Final 52000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	80.00 ft			
Tool Length:	108.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			3258.00	
Shut In Tool	5.00			3263.00	
Hydraulic tool	5.00			3268.00	
Jars	5.00			3273.00	
Safety Joint	3.00			3276.00	
Packer	4.00			3280.00	28.00 Bottom Of Top Packer
Packer	5.00			3285.00	
Stubb	1.00			3286.00	
Perforations	2.00			3288.00	
Change Over Sub	1.00			3289.00	
Recorder	0.00	8321	Inside	3289.00	
Recorder	0.00	8679	Outside	3289.00	
Drill Pipe	62.00			3351.00	
Change Over Sub	1.00			3352.00	
Perforations	10.00			3362.00	
Bullnose	3.00			3365.00	80.00 Bottom Packers & Anchor
Total Tool Length:	108.00				



Weatherford[®] Completion Systems

DRILL STEM TEST REPORT

FLUID SUMMARY

Berexco LLC
2020 N. Bramblewood
Wichita KS 67206-1094
ATTN: Bruce Meyer

Armbrister Unit #1
10-11s-19w Ellis,KS
Job Ticket: 090406 **DST#: 3**
Test Start: 2010.10.04 @ 20:33:43

Mud and Cushion Information

Mud Type: Gel Chem	Cushion Type:	Oil API:	deg API
Mud Weight: 9.00 lb/gal	Cushion Length: ft	Water Salinity:	80000 ppm
Viscosity: 60.00 sec/qt	Cushion Volume: bbl		
Water Loss: 9.17 in ³	Gas Cushion Type:		
Resistivity: ohm.m	Gas Cushion Pressure: psig		
Salinity: 4000.00 ppm			
Filter Cake: inches			

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
362.00	MW40%M60%W	1.780
82.00	WM40%W60%M	0.889

Total Length: 444.00 ft Total Volume: 2.669 bbl

Num Fluid Samples: 0 Num Gas Bombs: 0 Serial #:

Laboratory Name: Laboratory Location:

Recovery Comments:

