

Company	Falcon Exploration, Inc.	Lease Name	Van Blaricum NE	
Address	125 North Market, Suite 1252	Lease #	1-6	
CSZ	Wichita, KS 67202	Legal Desc	SE SE NW NE	Job Ticket 3465
Attn.	Tim Priest	Section	6	Range 30W
		Township	28S	
		County	Gray	State KS
		Drilling Cont	Val Drilling #1	


Comments **Field: Wildcat**

GENERAL INFORMATION

Test # 5	Test Date 2/27/2012	Chokes 3/4	Hole Size 7 7/8
Tester Jimmy Ricketts		Top Recorder # 13767	
Test Type Straddle		Mid Recorder # w1022	
		Bott Recorder # w1023	
# of Packers 3.0	Packer Size 6 3/4	Mileage 210	Approved By
		Standby Time 0	
Mud Type Gel Chem		Extra Equipmnt Jars, S.J. Extra Packer, 2 small packers	
Mud Weight 9.5	Viscosity 58.0	Time on Site 8:15 PM	
Filtrate 7.2	Chlorides 2800	Tool Picked Up 8:30 PM	
		Tool Layed Dwn 6:00 AM	
Drill Collar Len 0			
Wght Pipe Len 0		Elevation 2824.00	Kelley Bushings 2834.00
Formation Marrow Sand		Start Date/Time 2/27/2012 9:23 PM	
Interval Top 5078.0	Bottom 5159.0	End Date/Time 2/28/2012 7:01 AM	
Anchor Len Below 81.0	Between 0		
Total Depth 5393.0			
Blow Type Weak blow building to 1 inch initial flow period. Weak blow building to 1/4 inch final flow period. Times: 5, 90, 60, 90.			

RECOVERY

Feet	Description	Gas	Oil	Water	Mud
40	Drilling mud with trace oil	0% 0ft	trace	0% 0ft	100%40ft
DST Fluids	0				

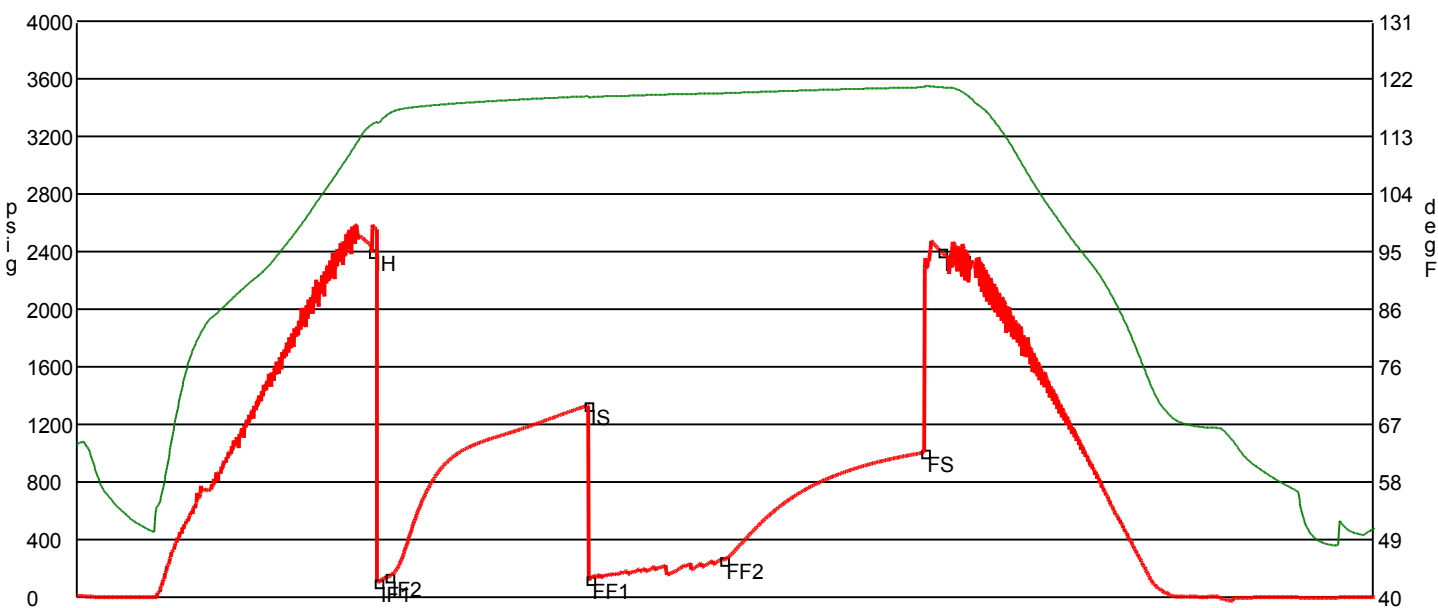

	Date	Time	Pressure	Temp	
IH	2/27/2012 11:32:45 PM	2.1625	2399.087	114.687	Initial Hydro-static
IF1	2/27/2012 11:35:30 PM	2.208333	103.973	114.952	Initial Flow (1)
IF2	2/27/2012 11:40:15 PM	2.2875	144.334	116.383	Initial Flow (2)
IS	2/28/2012 1:09:15 AM	3.770833	1333.201	119.188	Initial Shut-In
FF1	2/28/2012 1:10:15 AM	3.7875	126.234	119.015	Final Flow (1)
FF2	2/28/2012 2:10:00 AM	4.783333	260.472	119.665	Final Flow (2)
FS	2/28/2012 3:39:45 AM	6.279167	1005.696	120.601	Final Shut-In
FH	2/28/2012 3:47:30 AM	6.408333	2401.55	120.6	Final Hydro-static

GAS FLOWS

Min Into IFP Min Into FFP Gas Flows Pressure Choke
