



**Company: L. D. Drilling, Inc**  
**Lease: Wiles Trust #1-15**

SEC: 15 TWN: 16S RNG: 37W  
 County: WICHITA  
 State: Kansas  
 Drilling Contractor: L. D. Drilling, Inc - Rig 1  
 Elevation: 3352 EGL  
 Field Name: Wildcat  
 Pool: Infield  
 Job Number: 238

**Operation:**  
 Uploading recovery & pressures

**DATE**  
 October  
**30**  
 2018

**DST #3**    **Formation: Altamont**    **Test Interval: 4438 - 4530'**    **Total Depth: 4530'**

Time On: 09:09 10/30    Time Off: 15:26 10/30  
 Time On Bottom: 11:41 10/30    Time Off Bottom: 13:41 10/30

Electronic Volume Estimate:  
 14'


1st Open  
 Minutes: 30  
 Current Reading: 1" at 30 min  
 Max Reading: 1"

1st Close  
 Minutes: 30  
 Current Reading: 0" at 30 min  
 Max Reading: 0"

2nd Open  
 Minutes: 30  
 Current Reading: .1" at 30 min  
 Max Reading: .1"

2nd Close  
 Minutes: 30  
 Current Reading: 0" at 30 min  
 Max Reading: 0"

Inside Recorder

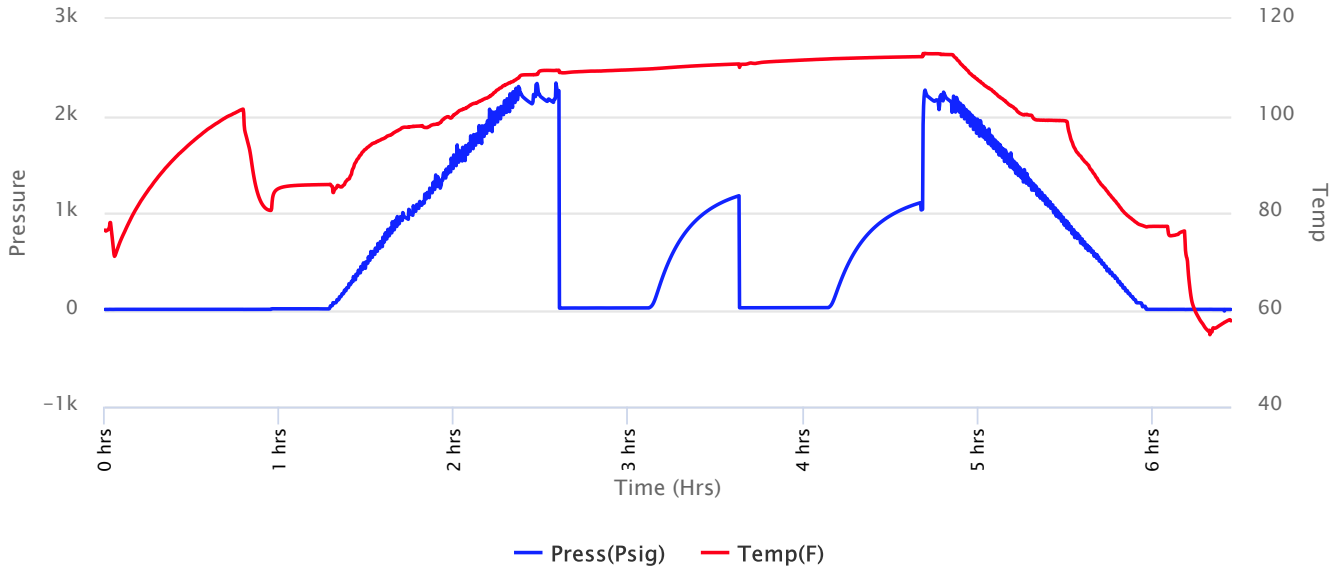



**Company: L. D. Drilling, Inc**  
**Lease: Wiles Trust #1-15**

SEC: 15 TWN: 16S RNG: 37W  
 County: WICHITA  
 State: Kansas  
 Drilling Contractor: L. D. Drilling, Inc - Rig 1  
 Elevation: 3352 EGL  
 Field Name: Wildcat  
 Pool: Infield  
 Job Number: 238

**Operation:**  
 Uploading recovery & pressures

**DATE**  
 October  
**30**  
 2018

**DST #3**    **Formation: Altamont**    **Test Interval: 4438 - 4530'**    **Total Depth: 4530'**  
 Time On: 09:09 10/30    Time Off: 15:26 10/30  
 Time On Bottom: 11:41 10/30    Time Off Bottom: 13:41 10/30


Recovered		Description of Fluid	Gas %	Oil %	Water %	Mud %
Foot	BBLs					
20	0.2052	M	0	0	0	100

Total Recovered: 20 ft  
 Total Barrels Recovered: 0.2052

**Reversed Out**  
**NO**

Initial Hydrostatic Pressure	2165	PSI
Initial Flow	17 to 19	PSI
<b>Initial Closed in Pressure</b>	<b>1171</b>	<b>PSI</b>
Final Flow Pressure	20 to 22	PSI
<b>Final Closed in Pressure</b>	<b>1101</b>	<b>PSI</b>
Final Hydrostatic Pressure	2165	PSI
Temperature	113	°F
Pressure Change Initial Close / Final Close	5.9	%

**Recovery at a glance**

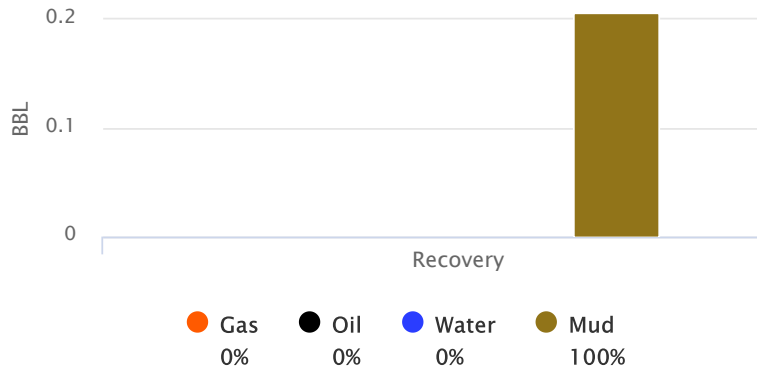



**Company: L. D. Drilling, Inc**  
**Lease: Wiles Trust #1-15**

SEC: 15 TWN: 16S RNG: 37W  
County: WICHITA  
State: Kansas  
Drilling Contractor: L. D. Drilling, Inc -  
Rig 1  
Elevation: 3352 EGL  
Field Name: Wildcat  
Pool: Infield  
Job Number: 238

**Operation:**  
Uploading recovery &  
pressures

**DATE**  
October  
**30**  
2018

**DST #3      Formation: Altamont      Test Interval: 4438 -      Total Depth: 4530'**  
**4530'**  
Time On: 09:09 10/30      Time Off: 15:26 10/30  
Time On Bottom: 11:41 10/30      Time Off Bottom: 13:41 10/30

**BUCKET MEASUREMENT:**

1st Open: 1/4" blow built to 1" in 30 min.  
1st Close: No Return  
2nd Open: Weak surface blow started at 20 min. Did not build or die.  
2nd Close: No return

**REMARKS:**

Slight Oil scum in tool sample.  
  
Tool Sample: 0% Gas 0% Oil 2% Water 98% Mud





**Company: L. D. Drilling, Inc**  
**Lease: Wiles Trust #1-15**

SEC: 15 TWN: 16S RNG: 37W  
County: WICHITA  
State: Kansas  
Drilling Contractor: L. D. Drilling, Inc -  
Rig 1  
Elevation: 3352 EGL  
Field Name: Wildcat  
Pool: Infield  
Job Number: 238

**Operation:**  
Uploading recovery &  
pressures

**DATE**  
October  
**30**  
2018

**DST #3      Formation: Altamont      Test Interval: 4438 -      Total Depth: 4530'**  
**4530'**

Time On: 09:09 10/30      Time Off: 15:26 10/30  
Time On Bottom: 11:41 10/30      Time Off Bottom: 13:41 10/30

**Mud Properties**

**Mud Type:** Chem      **Weight:** 9.4      **Viscosity:** 57      **Filtrate:** 9.6      **Chlorides:** 5000 ppm
