



TRILOBITE TESTING, INC.

DRILL STEM TEST REPORT

Primal Energy O&G, LLC.
 21021 Springbrook Plaza Dr.
 Spring, TX 77379
 ATTN: Justin Carter

28-18s-9w Rice Co., KS
Skiles 28-1
 Job Ticket: 51978 **DST#:4**
 Test Start: 2014.05.13 @ 09:27:57

GENERAL INFORMATION:


Formation: **Arbuckle**
 Deviated: No Whipstock: 0.00 ft (KB)
 Time Tool Opened: 10:59:42
 Time Test Ended: 17:44:12
 Interval: **3145.00 ft (KB) To 3239.00 ft (KB) (TVD)**
 Total Depth: 3239.00 ft (KB) (TVD)
 Hole Diameter: 7.88 inches Hole Condition: Fair
 Test Type: Conventional Bottom Hole (Reset)
 Tester: Ryan Reynolds
 Unit No: 68
 Reference Elevations: 1714.00 ft (KB)
 1706.00 ft (CF)
 KB to GR/CF: 8.00 ft

Serial #: 8790

Inside

Press@RunDepth: 849.25 psig @ 3151.00 ft (KB)
 Start Date: 2014.05.13 End Date: 2014.05.13
 Start Time: 09:27:57 End Time: 17:44:12
 Capacity: 8000.00 psig
 Last Calib.: 2014.05.13
 Time On Btm: 2014.05.13 @ 10:57:57
 Time Off Btm: 2014.05.13 @ 14:49:57

TEST COMMENT: IF: Strong blow. BOB @ 1min.
 ISI: Weak 2" BB
 FF: Strong blow. BOB @ 2min.
 FSI: No blow

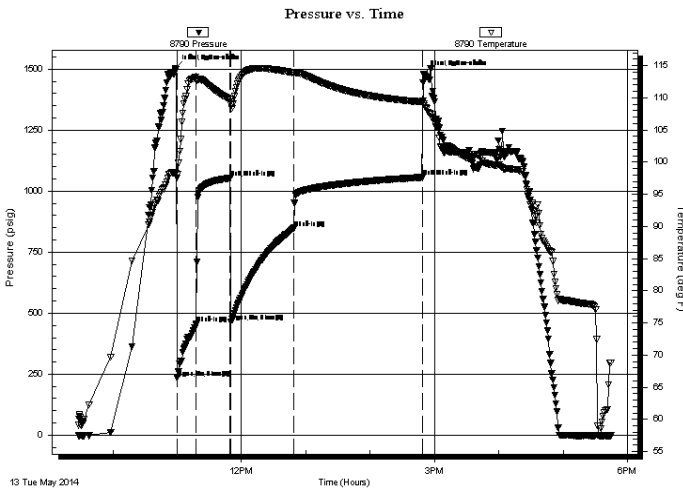

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1503.80	98.32	Initial Hydro-static
2	232.85	97.50	Open To Flow(1)
20	456.46	112.86	Shut-In(1)
52	1053.80	109.71	End Shut-In(1)
52	464.24	109.30	Open To Flow(2)
111	849.25	113.87	Shut-In(2)
231	1056.79	109.33	End Shut-In(2)
232	1480.13	109.06	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
2500.00	Clean Gassy Oil	18.56
0.00	120' GIP Rvsd approx. 20bbl. to truck	0.00

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)

* Recovery from multiple tests

Serial #: 8790


Inside

Primal Energy O&G, LLC.

Skiles 28-1

DST Test Number: 4

Pressure vs. Time

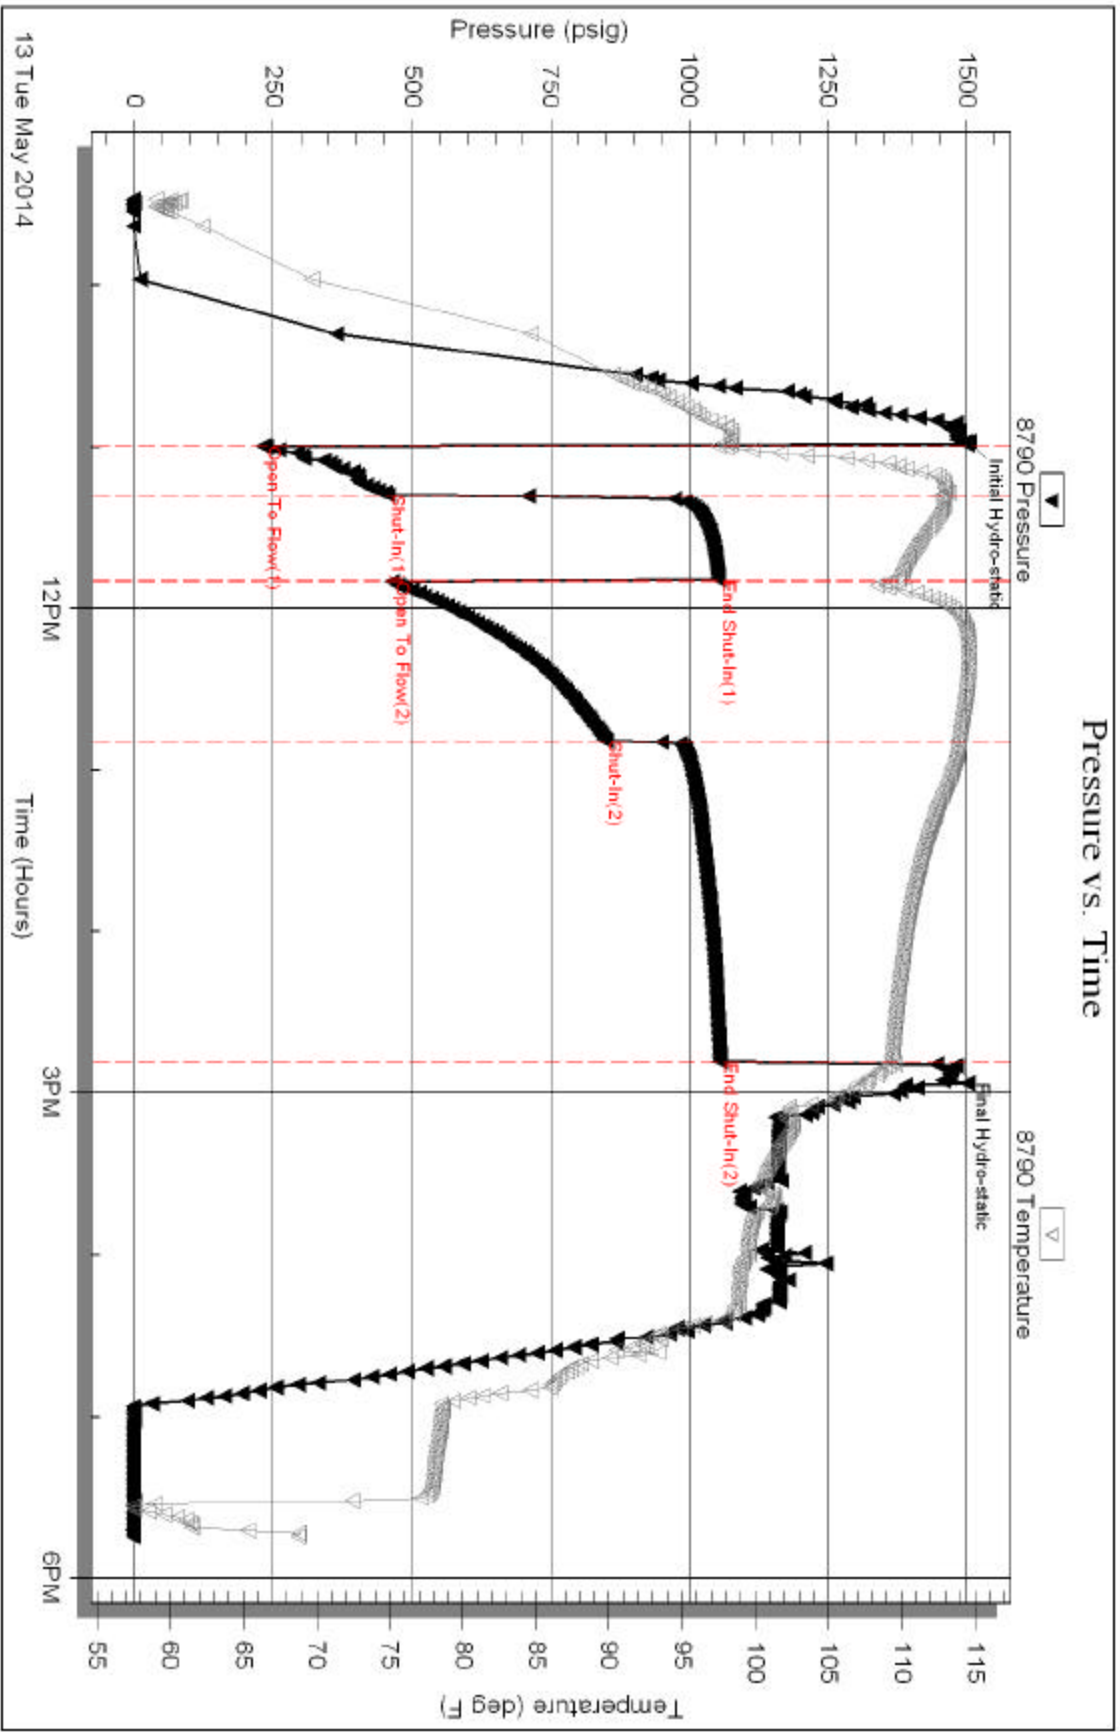

Trickle Testing, Inc

Ref. No: 51878

Printed: 2014.05.13 @ 18:05:01
