



TRILOBITE TESTING, INC.

DRILL STEM TEST REPORT

Concorde Resources Corp

27-15-34 Logan Ks

111 S. Main St.
Eufaula, Ok 74432

Reta 2-27

Job Ticket: 63862

DST#: 3

ATTN: Larry Nicholson

Test Start: 2017.07.31 @ 18:44:44

GENERAL INFORMATION:

Formation: **Pleas/ Alt- A**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 20:40:44

Time Test Ended: 00:12:44

Test Type: Conventional Bottom Hole (Reset)

Tester: Brandon Turley

Unit No: 79

Interval: 4288.00 ft (KB) To 4333.00 ft (KB) (TVD)

Reference Elevations: 2987.00 ft (KB)

Total Depth: 4333.00 ft (KB) (TVD)

2977.00 ft (CF)

Hole Diameter: 7.88 inches Hole Condition: Good

KB to GR/CF: 10.00 ft

Serial #: 8166 Outside

Press@RunDepth: 21.36 psig @ 4293.00 ft (KB)

Capacity: 8000.00 psig

Start Date: 2017.07.31

End Date:

2017.08.01

Last Calib.: 2017.08.01

Start Time: 18:44:49

End Time:

00:12:43

Time On Btm: 2017.07.31 @ 20:40:14


Time Off Btm: 2017.07.31 @ 21:55:14

TEST COMMENT: IF: Surface blow died in 6 min.

IS: No return.

FF: No blow.

Pulled tool

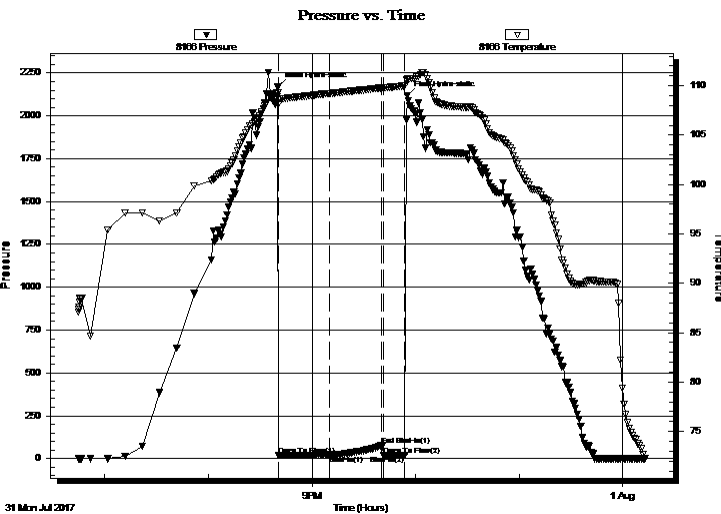

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2167.96	109.26	Initial Hydro-static
1	20.81	108.18	Open To Flow (1)
30	21.36	109.22	Shut-In(1)
60	75.90	109.77	End Shut-In(1)
61	21.09	109.77	Open To Flow (2)
74	20.63	109.99	Shut-In(2)
75	2116.54	110.72	Final Hydro-static


Recovery

Length (ft)	Description	Volume (bbl)
4.00	mud oil spots 100%m	0.06

* Recovery from multiple tests

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)

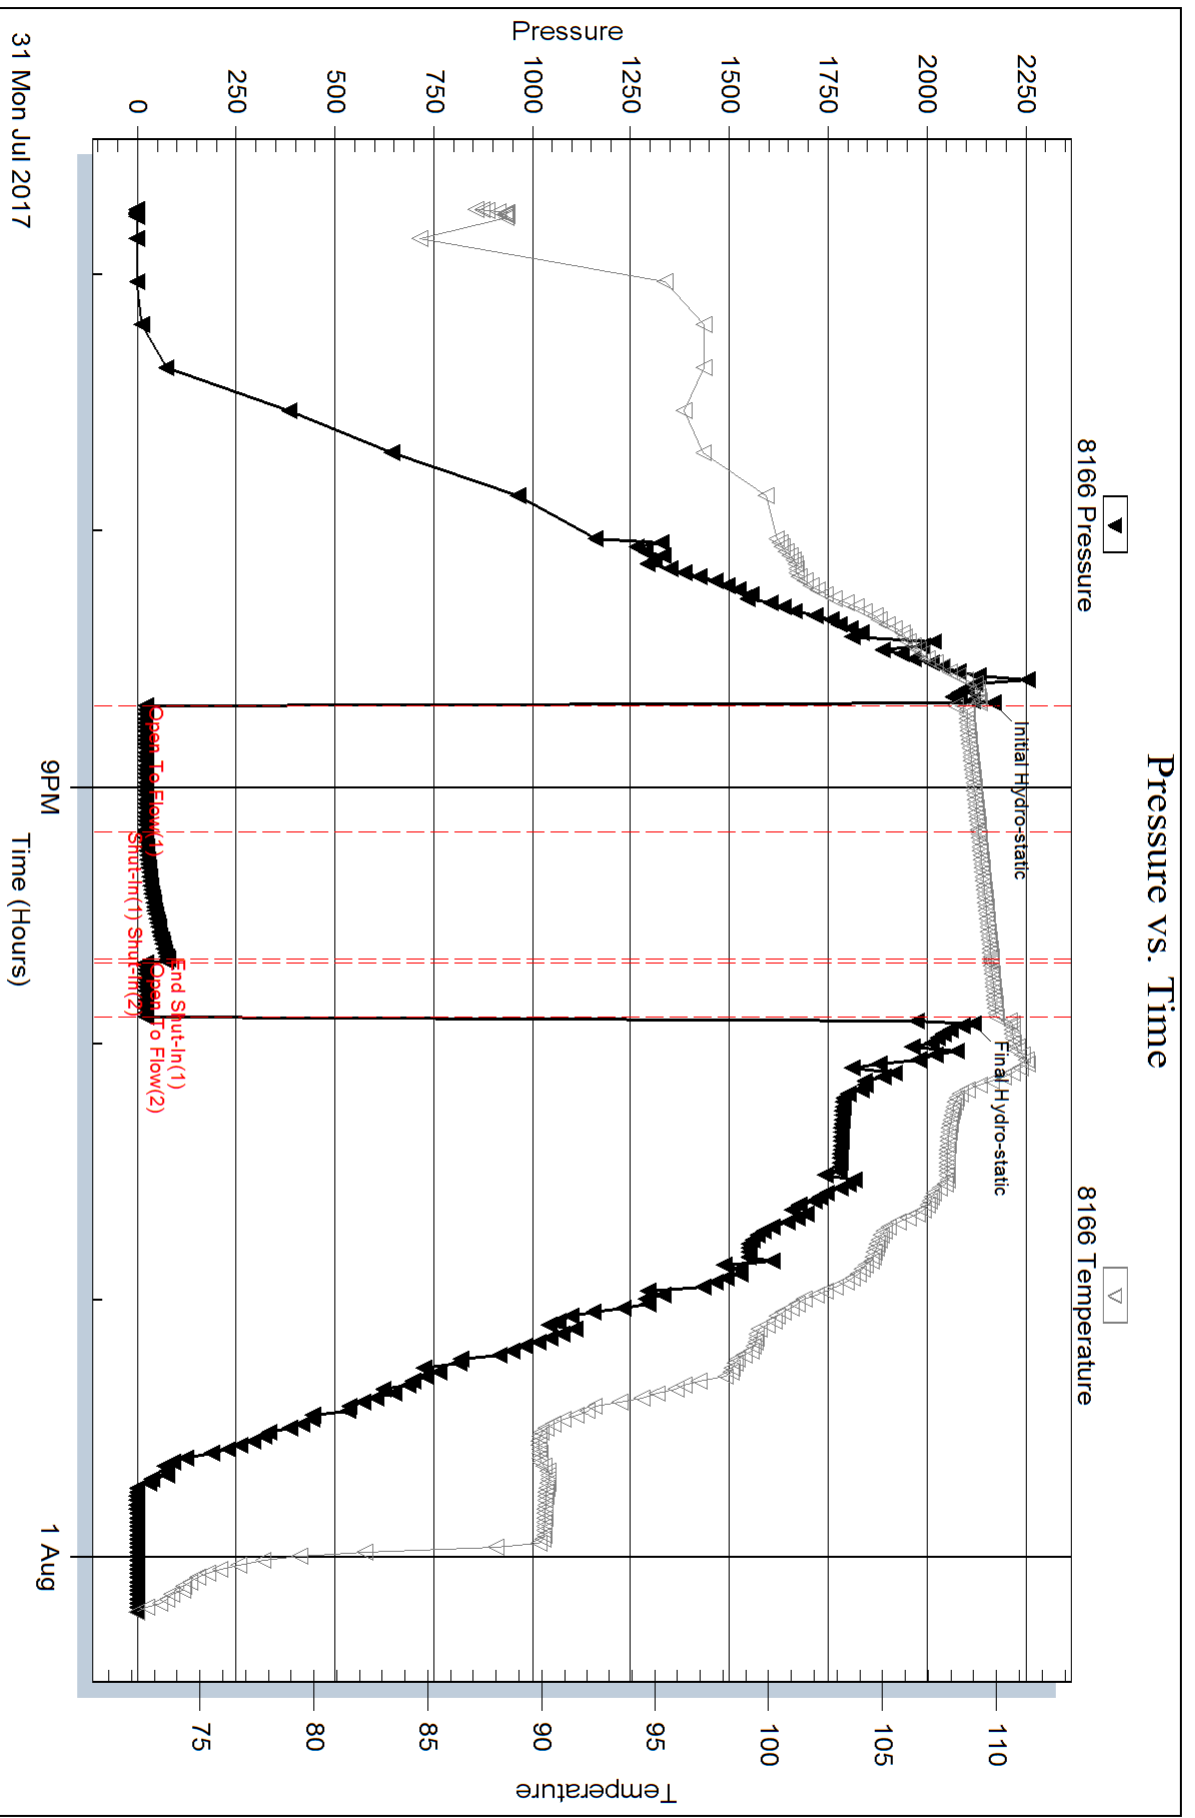

Serial #: 8875

Inside

Concorde Resources Corp

Reta 2-27

DST Test Number: 3

