



Company: Raydon Exploration, Inc

Lease: Linda Jo #1-22

SEC: 22 TWN: 33S RNG: 31W
 County: SEWARD
 State: Kansas
 Drilling Contractor: Quest Drilling Services, LLC - Rig 102
 Elevation: 2750 KB
 Field Name: Kismet
 Pool: WILDCAT
 Job Number: 21

DATE
August
07
2017

DST #8	Formation: Cherokee	Test Interval: 5386 - 5417'	Total Depth: 5417'
	Time On: 04:10 08/07	Time Off: 13:41 08/07	
	Time On Bottom: 06:50 08/07	Time Off Bottom: 11:20 08/07	


Electronic Volume Estimate:
208'

1st Open
Minutes: 30
1.9" at 30 min

1st Close
Minutes: 60
0" at 60 min

2nd Open
Minutes: 60
3.2" at 60 min

2nd Close
Minutes: 120
0" at 120 min

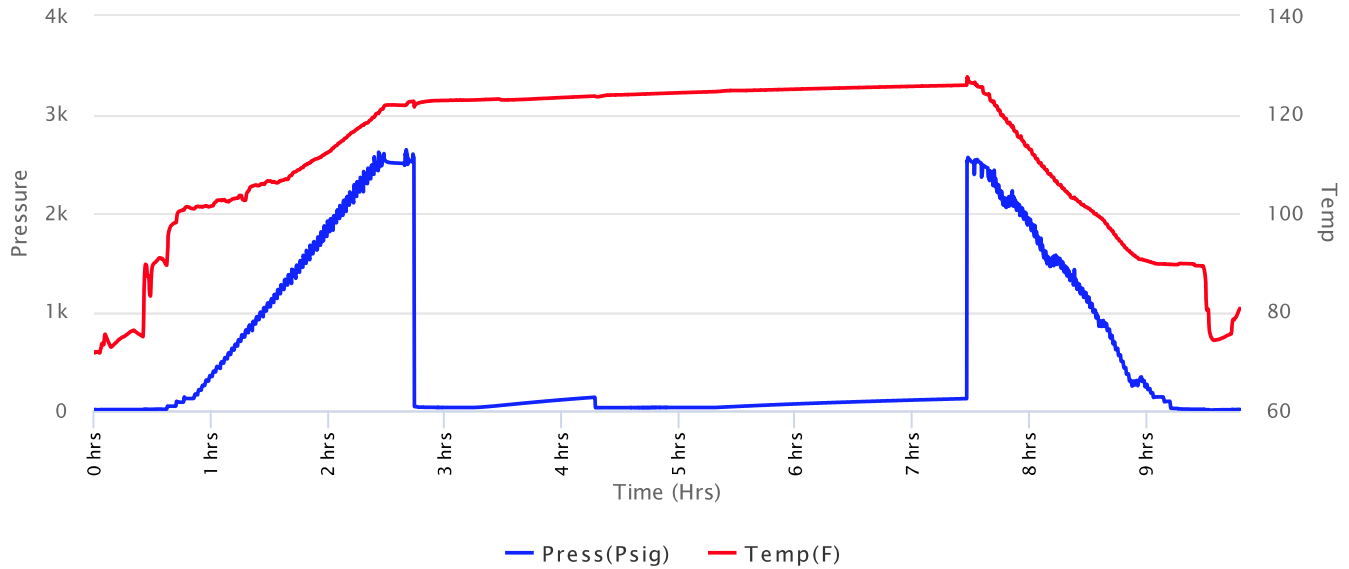



Company: Raydon Exploration, Inc

Lease: Linda Jo #1-22

SEC: 22 TWN: 33S RNG: 31W
 County: SEWARD
 State: Kansas
 Drilling Contractor: Quest Drilling Services, LLC - Rig 102
 Elevation: 2750 KB
 Field Name: Kismet
 Pool: WILDCAT
 Job Number: 21

DATE
August
07
2017

DST #8 **Formation: Cherokee** **Test Interval: 5386 - 5417'** **Total Depth: 5417'**

Time On: 04:10 08/07 Time Off: 13:41 08/07

Time On Bottom: 06:50 08/07 Time Off Bottom: 11:20 08/07

Recovered


Foot	BBLS	Description of Fluid	Gas %	Oil %	Water %	Mud %
40	0.1968	M	0	0	0	100

Total Recovered: 40 ft
 Total Barrels Recovered: 0.1968

Reversed Out
NO

Initial Hydrostatic Pressure	2506	PSI
Initial Flow	35 to 32	PSI
Initial Closed in Pressure	135	PSI
Final Flow Pressure	28 to 31	PSI
Final Closed in Pressure	121	PSI
Final Hydrostatic Pressure	2507	PSI
Temperature	126	°F
Pressure Change Initial Close / Final Close	10.2	%

Recovery at a glance

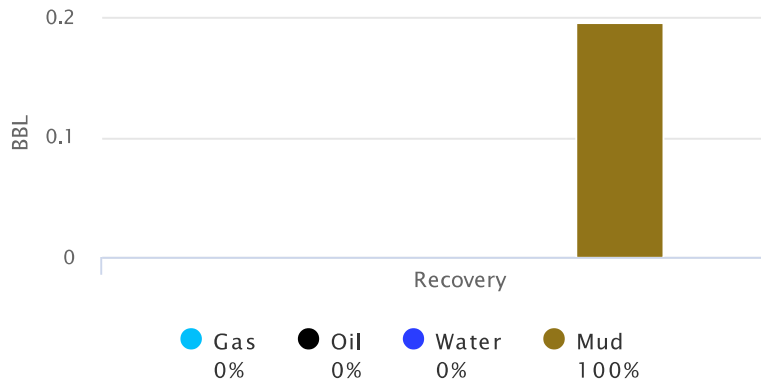



Company: Raydon Exploration, Inc

Lease: Linda Jo #1-22

SEC: 22 TWN: 33S RNG: 31W
County: SEWARD
State: Kansas
Drilling Contractor: Quest Drilling Services, LLC - Rig 102
Elevation: 2750 KB
Field Name: Kismet
Pool: WILDCAT
Job Number: 21

DATE August 07 2017
--

DST #8 **Formation: Cherokee** **Test Interval: 5386 - 5417'** **Total Depth: 5417'**
Time On: 04:10 08/07 Time Off: 13:41 08/07
Time On Bottom: 06:50 08/07 Time Off Bottom: 11:20 08/07

Down Hole Makeup

Heads Up: 14.4 FT	Packer 1: 5380.5 FT
Drill Pipe: 5099.21 FT <i>ID-3 1/2</i>	Packer 2: 5386 FT
Weight Pipe: 0 FT <i>ID-2 7/8</i>	Top Recorder: 5369.92 FT
Collars: 268.12 FT <i>ID-2 1/4</i>	Bottom Recorder: 5388 FT
Test Tool: 34.07 FT <i>ID-3 1/2-FH</i> <i>Jars</i> <i>Safety Joint</i>	Well Bore Size: 7 7/8
Total Anchor: 31	Surface Choke: 1"
	Bottom Choke: 5/8"

Anchor Makeup

Packer Sub: 1 FT

Perforations: (top): FT
4 1/2-FH

Change Over: FT

Drill Pipe: (in anchor): FT
ID-3 1/2

Change Over: FT

Perforations: (below): 30 FT
4 1/2-FH



**Company: Raydon Exploration,
Inc**

Lease: Linda Jo #1-22

SEC: 22 TWN: 33S RNG: 31W
County: SEWARD
State: Kansas
Drilling Contractor: Quest Drilling
Services, LLC - Rig 102
Elevation: 2750 KB
Field Name: Kismet
Pool: WILDCAT
Job Number: 21

DATE August 07 2017
--

DST #8	Formation: Cherokee	Test Interval: 5386 - 5417'	Total Depth: 5417'
	Time On: 04:10 08/07	Time Off: 13:41 08/07	
	Time On Bottom: 06:50 08/07	Time Off Bottom: 11:20 08/07	

Mud Properties

Mud Type: Chemical **Weight:** 8.7 **Viscosity:** 51 **Filtrate:** 6.4 **Chlorides:** 5000 ppm
