DRILL STEM TEST REPORT

TRILOBITE TESTING, INC.

Brito Oil Co Inc

1700 N Waterfront PKWY Bldg 300 Suite C
Wichita ,Ks 67206

ATTN: Brad Rine

Jennison UInit #1-32

32-16s-29w Lane,Ks

Job Ticket: 040712 DST#: 4

Test Start: 2011.03.04 @ 06:50:28

GENERAL INFORMATION:

Formation: **Ft Scott,Cherokee**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 08:47:00
Time Test Ended: 11:13:28

Test Type: Conventional Bottom Hole
Tester: Shane McBride
Unit No: 55

Interval: 4403.00 ft (KB) To 4453.00 ft (KB) (TVD)
Total Depth: 4453.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2775.00 ft (KB)
2770.00 ft (CF)
KB to GR/CF: 5.00 ft

Serial #: 6771 **Outside**

Press@RunDepth: psig @ 4404.00 ft (KB)
Start Date: 2011.03.04 End Date: 2011.03.04
Start Time: 06:50:28 End Time: 11:13:28

Capacity: 8000.00 psig
Last Calib.: 2011.03.04
Time On Btm: 2011.03.04 @ 08:54:43
Time Off Btm: 2011.03.04 @ 08:57:28

TEST COMMENT: packers failed @ open reset failed again pull tool

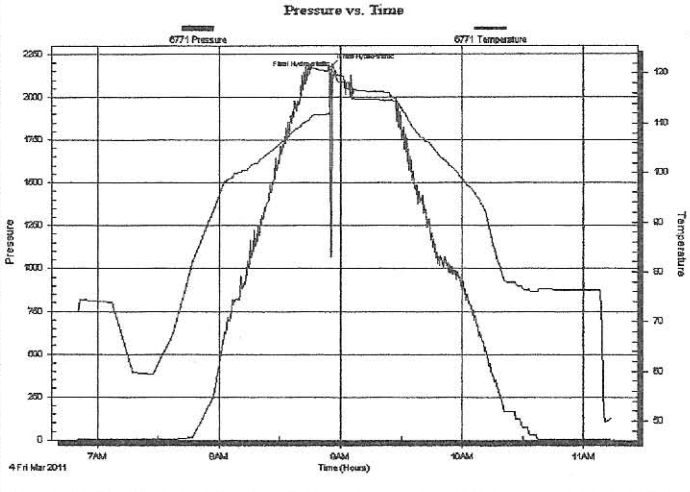

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2171.33	111.83	Initial Hydro-static
3	2129.35	119.64	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
330.00	mud 100%m	4.63

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
