DRILL STEM TEST REPORT

F.G.Holl Company L.L.C.

9431 East Central Suite 100
Wichita,Kansas 67206

ATTN: Ryan Greenbaum

Romine Trust #2-1

1-20s-15w Barton

Job Ticket: 16492 **DST#: 5**

Test Start: 2011.05.19 @ 10:00:00

GENERAL INFORMATION:

Formation: **Conglomerate**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 00:00:00
Time Test Ended: 00:00:00

Test Type: Conventional Bottom Hole (Initial)
Tester: Gene Budig
Unit No: 3325

Interval: 3510.00 ft (KB) To 3600.00 ft (KB) (TVD)
Total Depth: 3600.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1963.00 ft (KB)
1955.00 ft (CF)
KB to GR/CF: 8.00 ft

Serial #: 8525 **Outside**

Press@RunDepth:	84.04 psia @	3596.93 ft (KB)		Capacity:	5000.00 psia
Start Date:	2011.05.19	End Date:	2011.05.19	Last Calib.:	2011.05.19
Start Time:	10:01:00	End Time:	14:38:30	Time On Btm:	2011.05.19 @ 11:16:30
				Time Off Btm:	2011.05.19 @ 13:33:00

TEST COMMENT:
1st Opening 30 Minutes-Weak blow built to 1 inch into the w ater and decreased and died in 24 minutes
1st Shut-In 60 Minutes-No blow back
2nd opening 15 Minutes-No blow
2nd Shut-In 30 Minutes-No blow back

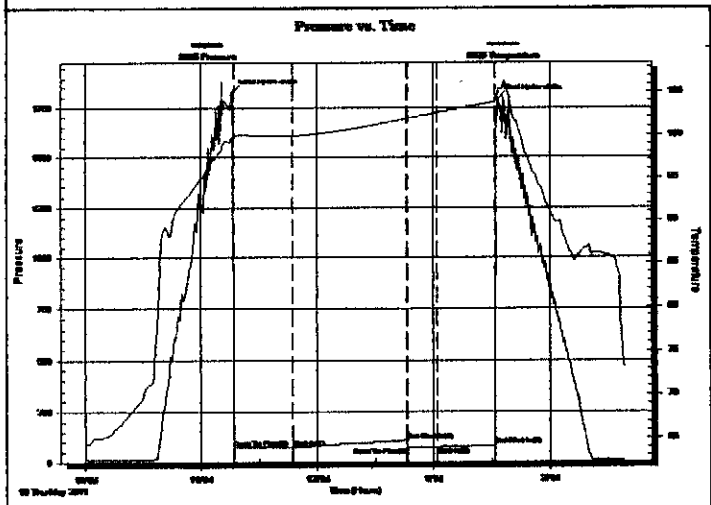

PRESSURE SUMMARY

Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	1829.13	99.79	Initial Hydro-static
1	72.27	99.67	Open To Flow (1)
31	75.02	99.87	Shut-In(1)
90	108.80	101.84	End Shut-In(1)
90	74.49	101.86	Open To Flow (2)
106	75.23	102.55	Shut-In(2)
135	84.04	103.83	End Shut-In(2)
137	1793.01	105.21	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
10.00	Drilling mud	0.14

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
