DRILL STEM TEST REPORT

F.G.Holl Company L.L.C.

9431 East Central Suite 100
Wichita,Kansas 67206

ATTN: Ryan Greenbaum

Romine Trust #2-1

1-20s-15w Barton

Job Ticket: 16493 **DST#: 6**

Test Start: 2011.05.20 @ 11:25:00

GENERAL INFORMATION:

Formation: **Conglomerate Sand**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 00:00:00
Time Test Ended: 00:00:00

Test Type: Conventional Bottom Hole (Initial)
Tester: Gene Budig
Unit No: 3325

Interval: 3555.00 ft (KB) To 3635.00 ft (KB) (TVD)
Total Depth: 3635.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1963.00 ft (KB)
1955.00 ft (CF)
KB to GR/CF: 8.00 ft

Serial #: 8524 **Inside**

Press@RunDepth:	144.68 psia @	3630.88 ft (KB)		Capacity:	5000.00 psia
Start Date:	2011.05.20	End Date:	2011.05.20	Last Calib.:	2011.05.20
Start Time:	11:26:00	End Time:	15:46:30	Time On Btm:	2011.05.20 @ 12:57:30
				Time Off Btm:	2011.05.20 @ 14:28:30

TEST COMMENT:
1st Opening 15 Minutes-Weak blow for 9 minutes
1st Shut-In 30 Minutes-No blow back
2nd Opening 15 Minutes-No blow
2nd Shut-In 30 Minutes-No blow back

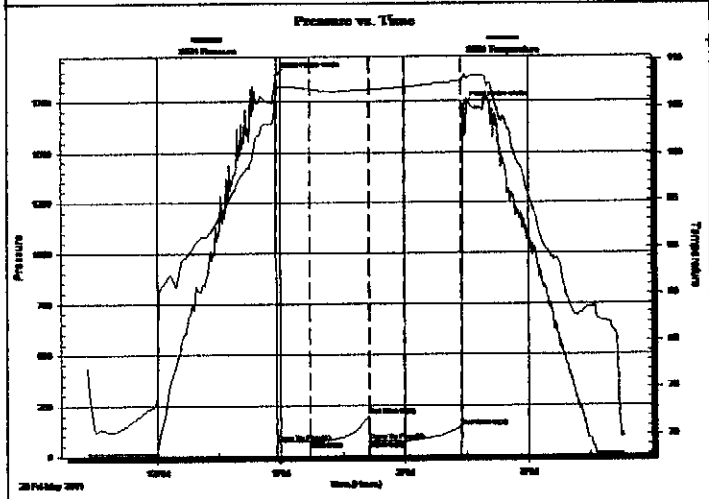

PRESSURE SUMMARY

Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	1881.11	106.67	Initial Hydro-static
1	69.41	106.94	Open To Flow (1)
17	71.46	106.95	Shut-In(1)
45	197.42	106.88	End Shut-In(1)
46	72.47	106.89	Open To Flow (2)
62	72.60	107.16	Shut-In(2)
90	144.68	107.81	End Shut-In(2)
91	1728.19	108.27	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
15.00	Drilling mud	0.21

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
