DRILL STEM TEST REPORT

F.G.Holl Company L.L.C.

9431 East Central Suite 100
Wichita,Kansas 67206

ATTN: Ryan Greenbaum

Romine Trust #2-1

1-20s-15w Barton

Job Ticket: 16494 **DST#:7**

Test Start: 2011.05.20 @ 12:30:00

GENERAL INFORMATION:

Formation: **Arbuckle**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 00:00:00
Time Test Ended: 00:00:00

Test Type: Conventional Bottom Hole (Initial)
Tester: Gene Budig
Unit No: 3335

Interval: 3555.00 ft (KB) To 3654.00 ft (KB) (TVD)
Total Depth: 3694.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1963.00 ft (KB)
1955.00 ft (CF)
KB to GR/CF: 8.00 ft

Serial #: 8525 **Outside**

Press@RunDepth:	216.52 psia @	3650.88 ft (KB)		Capacity:	5000.00 psia
Start Date:	2011.05.20	End Date:	2011.05.20	Last Calib.:	2011.05.20
Start Time:	12:31:00	End Time:	18:01:30	Time On Btm:	2011.05.20 @ 13:43:30
				Time Off Btm:	2011.05.20 @ 16:33:30

TEST COMMENT:
1st Opening 15 Minutes Weak blow built to 4 inches and decresed
1st Shut-In 60 Minutes-No blow back
2nd Opening 30 Minutes-Weak blow for 8 minutes and died
2nd Shut-In 60 Minutes-No blow back

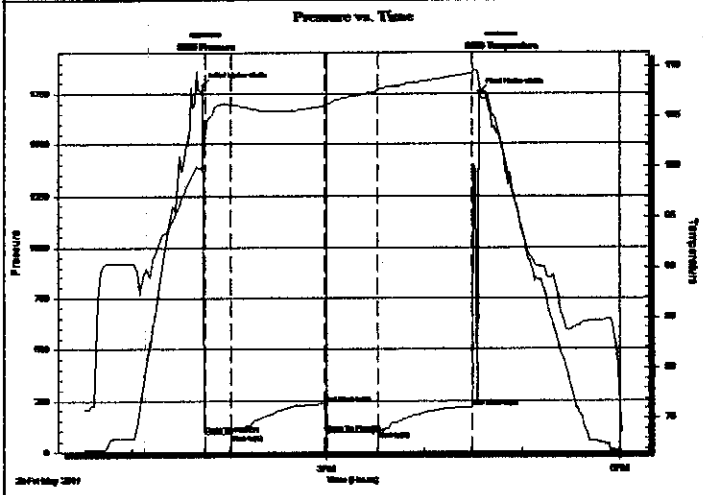

PRESSURE SUMMARY

Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	1788.68	100.17	Initial Hydro-static
2	87.57	103.41	Open To Flow (1)
17	88.23	106.19	Shut-In(1)
75	233.90	106.03	End Shut-In(1)
76	91.62	106.15	Open To Flow (2)
108	100.88	107.61	Shut-In(2)
166	216.52	109.30	End Shut-In(2)
170	1756.79	108.12	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
40.00	Drilling mud with a show of oil between	0.56
0.00	the tools	0.00

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
