DRILL STEM TEST REPORT

F.G.Holl Company L.L.C.

9431 East Central Suite 100
Wichita,Kansas 67206

ATTN: Ryan Greenbaum

Romine Trust #2-1

1-20s-15w Barton

Job Ticket: 16498 **DST#: 11**

Test Start: 2011.05.22 @ 01:15:00

GENERAL INFORMATION:

Formation: **Quartzite**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 00:00:00
Time Test Ended: 00:00:00

Interval: 3692.00 ft (KB) To 3717.00 ft (KB) (TVD)
Total Depth: 3717.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Test Type: Conventional Bottom Hole (Initial)
Tester: Gene Budig
Unit No: 3335

Reference Elevations: 1963.00 ft (KB)
1955.00 ft (CF)
KB to GR/CF: 8.00 ft

Serial #: 8525 **Outside**

Press@RunDepth:	42.85 psia @	3714.00 ft (KB)		Capacity:	5000.00 psia
Start Date:	2011.05.22	End Date:	2011.05.22	Last Calib.:	2011.05.22
Start Time:	01:16:00	End Time:	05:32:00	Time On Btm:	2011.05.22 @ 02:30:00
				Time Off Btm:	2011.05.22 @ 04:00:30

TEST COMMENT:
1st Opening 15 Minutes-very weak surface blow for 7 minutes and died
1st Shut-In 30 Minutes-No blow back
2nd Opening 15 Minutes-No blow
2nd Shut-In 30 Minutes-No blow back

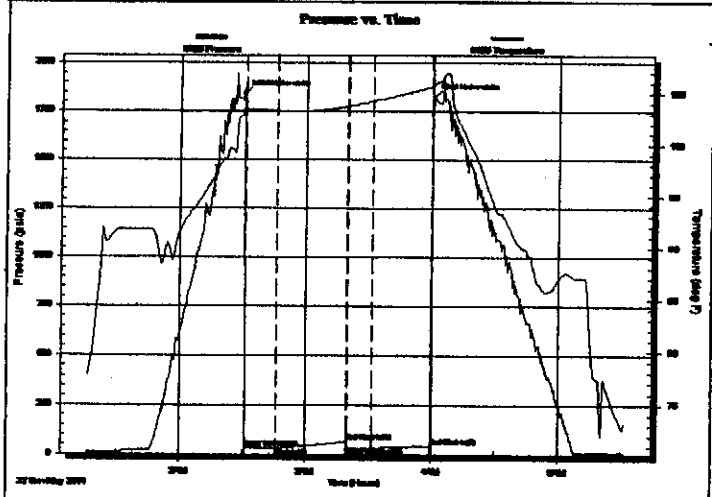

PRESSURE SUMMARY

Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	1839.17	103.38	Initial Hydro-static
1	32.23	103.39	Open To Flow (1)
16	32.73	103.32	Shut-In(1)
50	64.77	103.74	End Shut-In(1)
50	33.36	103.75	Open To Flow (2)
62	32.90	104.24	Shut-In(2)
90	42.85	105.64	End Shut-In(2)
91	1825.14	105.83	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
1.00	Oil cut mud 1%Oil 99%Mud	0.01

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
