DRILL STEM TEST REPORT

TRILOBITE TESTING, INC.

Lachenmayr Oil
PO Box 526
Newton, KS 67114

ATTN: Frank Mize

17-17S-19W Rush,KS

JME Farms #1

Job Ticket: 57956 **DST#: 2**

Test Start: 2016.10.17 @ 13:02:12

GENERAL INFORMATION:

Formation: **Arbuckle**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 15:07:57
Time Test Ended: 20:12:12

Test Type: Conventional Bottom Hole (Reset)
Tester: Leal Cason
Unit No: 74

Interval: 3867.00 ft (KB) To 3895.00 ft (KB) (TVD)
Total Depth: 3895.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2156.00 ft (KB)
2148.00 ft (CF)
KB to GR/CF: 8.00 ft

Serial #: 6806 **Outside**

Press@RunDepth:	psig @	3868.00 ft (KB)		Capacity:	8000.00 psig
Start Date:	2016.10.17	End Date:	2016.10.17	Last Calib.:	2016.10.17
Start Time:	13:02:13	End Time:	20:11:57	Time On Btm:	
				Time Off Btm:	

TEST COMMENT: IF: Weak 1/4 inch Blow
ISI: No Blow Back
FF: Weak 1/4 inch Blow
FSI: No Blow Back

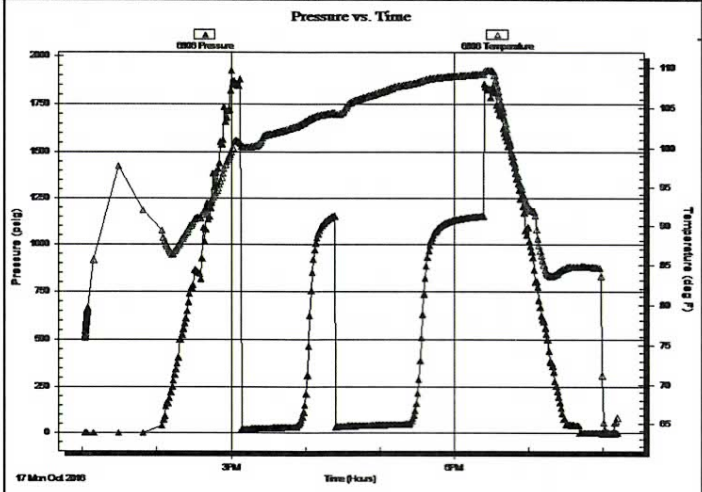

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation

Recovery

Length (ft)	Description	Volume (bbl)
60.00	OCM 30%O 70%M	0.84
5.00	Oil	0.07

* Recovery from multiple tests

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
