DRILL STEM TEST REPORT

FG Holl Company LLC

9431 East Central
Suite 100
Wichita, Kansas 67206+2563
ATTN: Renee Hustead

Reece Unit #1-32

32/22S/21W/Hodgeman

Job Ticket: 18787 **DST#: 1**

Test Start: 2011.10.21 @ 01:02:00

GENERAL INFORMATION:

Formation: **Marmaton**
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 03:01:30
Time Test Ended: 06:45:30

Interval: 4268.00 ft (KB) To 4337.00 ft (KB) (TVD)
Total Depth: 4337.00 ft (KB) (TVD)
Hole Diameter: 7.88 inches Hole Condition: Fair

Test Type: Conventional Bottom Hole (Initial)
Tester: Ken Swinney
Unit No: 3325 Great Bend/112

Reference Elevations: 2234.00 ft (KB)
2224.00 ft (CF)
KB to GR/CF: 10.00 ft

Serial #: 6749 **Outside**

Press@RunDepth:	73.51 psig @	4333.99 ft (KB)		Capacity:	5000.00 psig
Start Date:	2011.10.21	End Date:	2011.10.21	Last Calib.:	2011.10.21
Start Time:	01:03:00	End Time:	06:45:30	Time On Btm:	2011.10.21 @ 02:59:00
				Time Off Btm:	2011.10.21 @ 04:39:30

TEST COMMENT:
1ST Open 15 Minutes/Weak blow /Blow built to 1/2 inch
1ST Shut In 30 Minutes/No blow back
2ND Open 15 Minutes/No blow
2ND Shut In 30 Minutes/No blow back

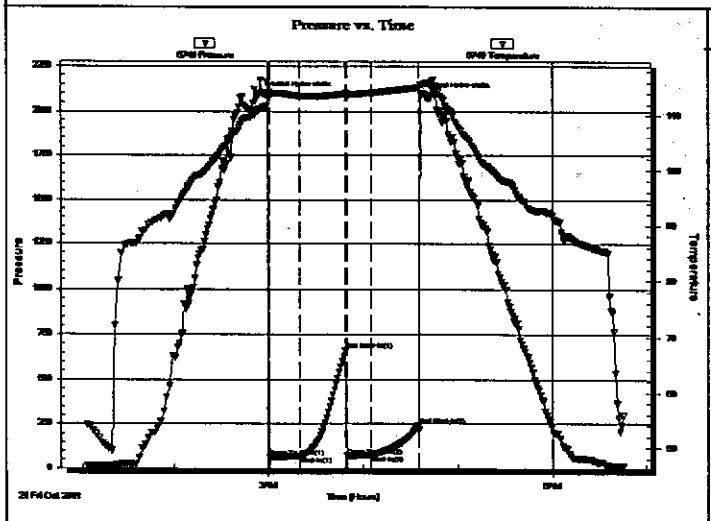

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2089.15	111.67	Initial Hydro-static
3	63.75	113.67	Open To Flow (1)
21	68.08	113.54	Shut-In(1)
51	662.99	113.91	End Shut-In(1)
52	71.10	113.77	Open To Flow (2)
66	73.51	114.08	Shut-In(2)
96	240.38	115.03	End Shut-In(2)
101	2081.99	115.80	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	Mud 100%	0.02

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)

Serial #: 6749 **Outside** FG Holl Company LLC 32/22S/21W/Hodgeman DST Test Number: 1

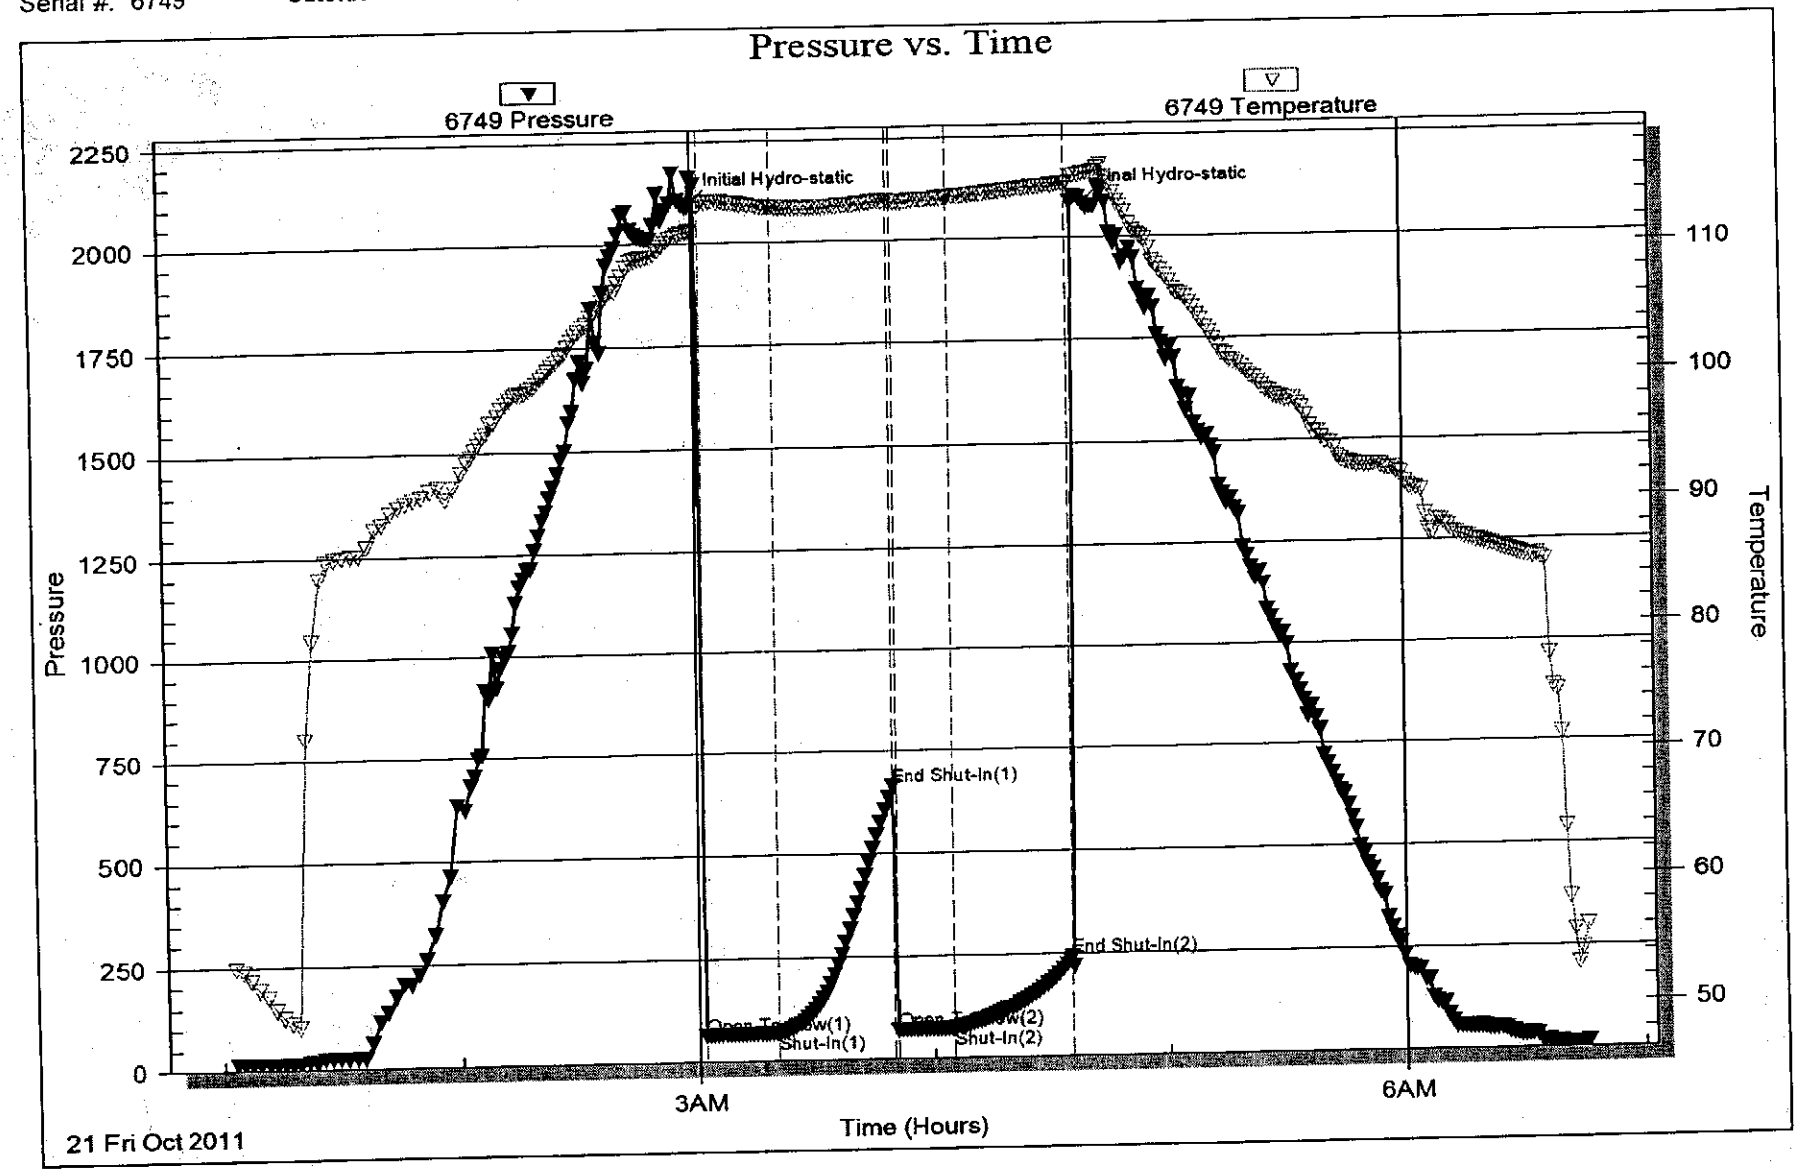

Superior Testers Enterprises LLC Ref. No: 18787 Printed: 2011.10.25 @ 09:08:10

Serial #: 6651 Inside FG Holl Company LLC 32/22S/21W/Hodgeman DST Test Number: 1

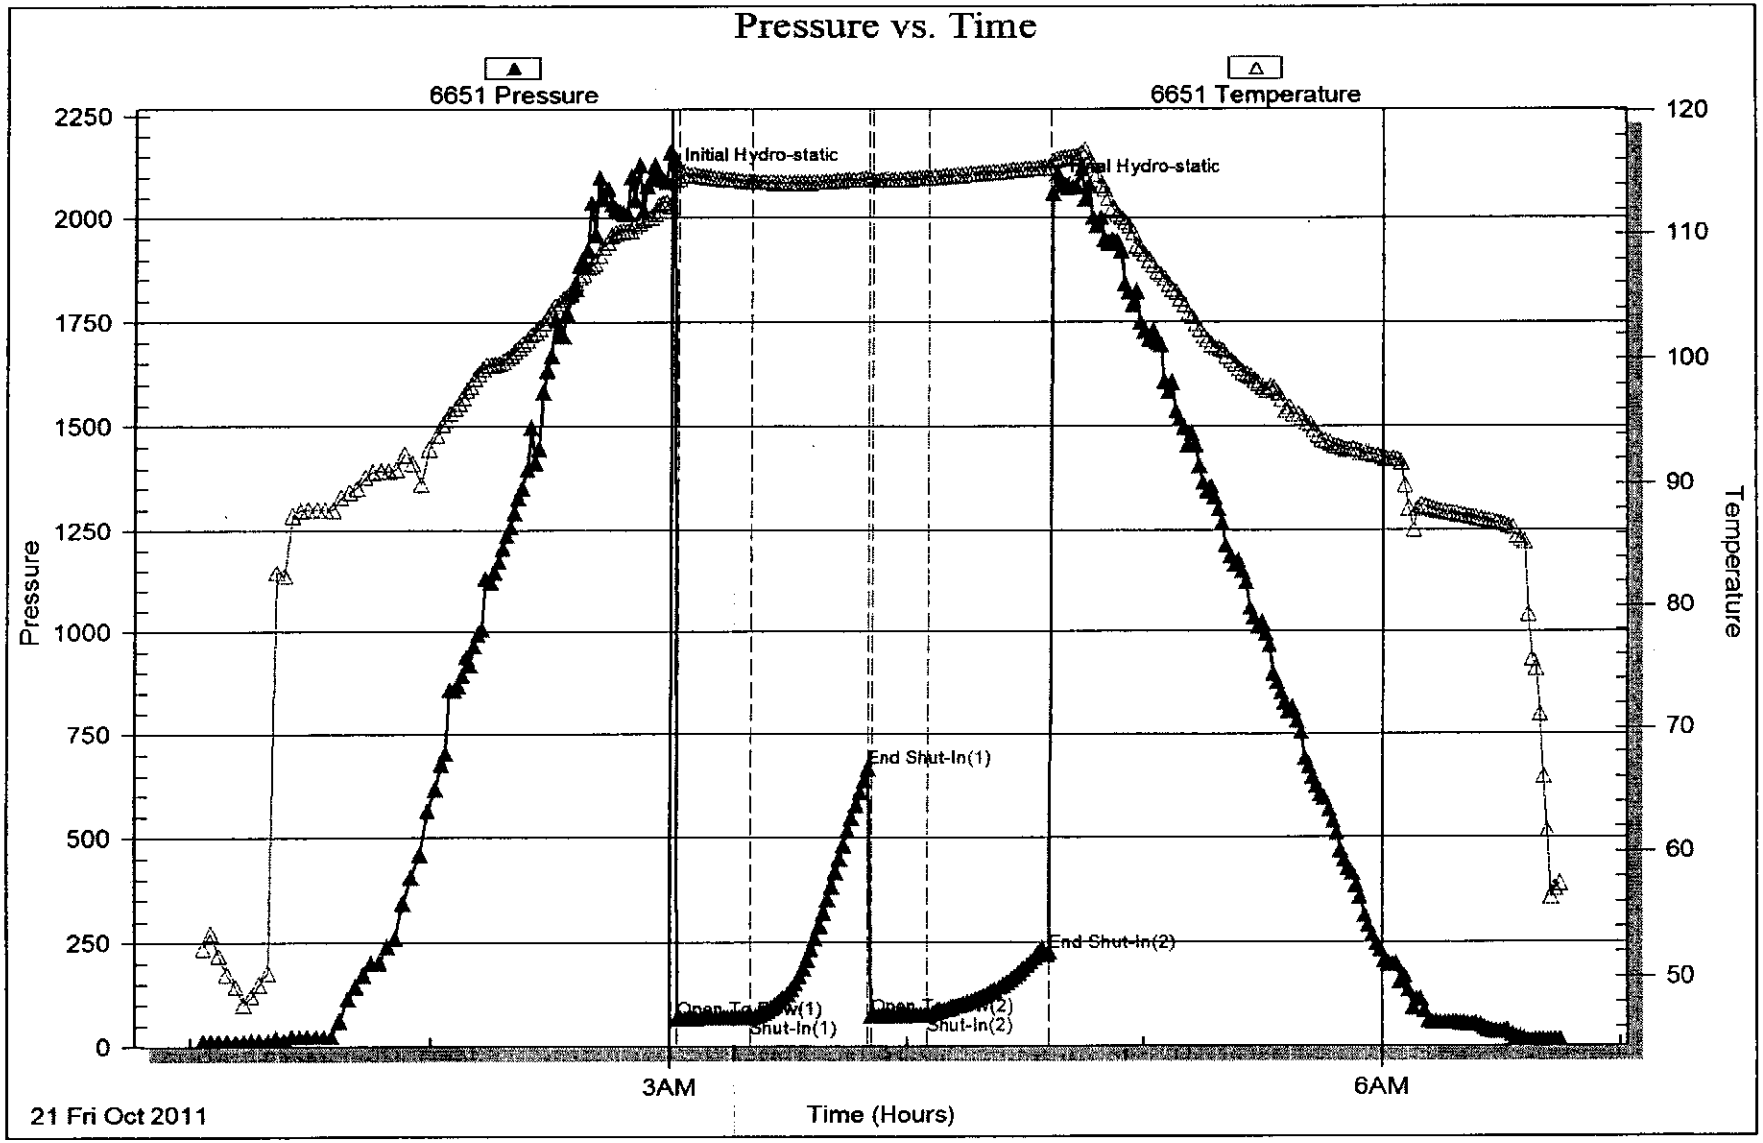

Superior Testers Enterprises LLC Ref. No: 18787 Printed: 2011.10.25 @ 09:08:10
